DHRMS IMPLEMENTATION PROJECT PLAN

Project Name: Datafin Human Resource Management System (DHRMS)
Objective: To develop and deploy a centralized, web-based HRMS that automates core HR functions, as outlined in the system description.

Core Modules

A web-based HRMS covering the following core modules as outlined in the system description:

- Employee Information Management
- Recruitment & Onboarding (ATS + offer/onboarding workflows)
- Attendance & Leave Management (attendance integration hooks)
- Payroll Management (core salary calc, statutory deductions, payslips)
- Performance Management (basic goals & appraisals)
- Training & Development (basic course tracking)
- Employee Self-Service Web Portal (profile, leave requests, payslips)
- Reports & Dashboards (headcount, leave trends, payroll cost)

High-level phases & timeline

1. System Architecture & Design – 1 week
   a. Activities:
      - Creating the Architecture Diagram.
      - Creating the Database Schema and ER Diagram.
      - Writing the Technical Design Document (TDD).
      - Creating API Documentation.

   b. Deliverables:
      - Architecture Diagram
      - Database Schema / ER Diagram

- Technical Design Document (TDD)
- API Documentation

2. Core Development – 17 weeks
   a. Split into sprints:
      - Sprint A: Dev Environment & Github Repository Setup
      - Sprint B: Employee Information Management + Auth
      - Sprint C: Attendance & Leave Management (including integration hooks)
      - Sprint D: Payroll core (salary calc, statutory deductions, payslip gen)
      - Sprint E: Recruitment & Onboarding (job post, ATS, offer letter)
      - Sprint F: Performance Management + Training modules
      - Sprint G: Employee Self-Service portal + Reports & Dashboards
      - Sprint I: Integration with external systems
      - Sprint J: Role-based Access Control (RBAC)

   b. Deliverables per sprint:
      - Working features, API docs, unit tests.

3. Integration & End-to-End Testing – 1 week
   a. Activities:
      - Run E2E Tests
      - Security & Performance Checks
      - Code adjustments based on E2E test outcome

4. UAT (User Acceptance Testing) – 1 week
   a. Activities:
      - HR and management users validate flows
      - Feedback cycle
      - Bug fixes

5. Deployment & Rollout – 1 week
   a. Activities:
      - Production deployment
      - Migration scripts
      - Final smoke tests
      - Training for HR staff.

6. Hypercare & Post-Deployment Support — continuous
   a. Activities:
      - Monitoring

- Fix high-priority issues
- Knowledge transfer
- Documentation handover.

Project Milestones

M1: Project Kickoff (Week 1)
- System Architecture & Design complete
- Development environment and GitHub repository setup plan approved

M2: Sprint A – Dev Environment & GitHub Repository Setup (Week 2)
- Development environment configured (backend, frontend, database)
- Version control, CI/CD, and branching strategy established
- Base project structure committed and tested

M3: Sprint B – Employee Information Management + Authentication (Week 3)
- Employee management module implemented (CRUD, profile upload)
- User authentication (login, password reset, session handling) completed
- API documentation and unit tests delivered

M4: Sprint C – Attendance & Leave Management (Week 5)
- Attendance tracking and leave request workflows implemented
- Integration hooks for external attendance systems
- Leave accrual, approval, and notification logic completed

M5: Sprint D – Payroll Core (Week 7)
- Salary computation logic, statutory deductions, and payslip generation
- Payroll export functions and reporting endpoints
- Validation and calculation accuracy tests completed

M6: Sprint E – Recruitment & Onboarding (Week 9)
- Job posting, applicant tracking, and interview scheduling workflows
- Offer letter generation and onboarding checklist setup
- Candidate data integrated into employee records

M7: Sprint F – Performance Management & Training (Week 11)
- Goal setting, appraisal templates, and evaluation flows
- Training module for course creation, assignment, and completion tracking

M8: Sprint G – Employee Self-Service Portal + Reports & Dashboards (Week 13)
- Self-service features (profile update, leave, payslips)
- Dashboard and analytical reports for HR and management users
- Export options (CSV, PDF) integrated

M9: Sprint I – Integration with External Systems (Week 15)
- Connect HRMS to external systems (payroll export, ERP)
- Data synchronization and validation testing

M10: Sprint J – Role-Based Access Control (RBAC) (Week 17)
- Define user roles and permissions
- Implement role-based access across all modules
- Access control tested for compliance and data protection

M11: UAT & Final Review (Week 19)
- End-to-end testing and bug fixes
- User acceptance testing completed and approved by HR stakeholders

M12: Production Deployment & Go-Live (Week 21)
- System deployed to production environment
- Documentation handover, training, and post-launch support

Deliverables (per module)

1. Employee information:
   - DB schema
   - CRUD APIs
   - File/document upload
   - Unique employee ID

2. Recruitment:
   - Job posting UI
   - Applicant tracking
   - Interview scheduling
   - Onboarding workflow

3. Attendance/Leave:
   - Integration endpoints

- Accrual & approval workflows
- Leave calendar

4. Payroll:
   - Salary computation engine
   - Statutory deductions
   - Payslip generation
   - Export to accounting

5. Performance:
   - Goal-setting
   - appraisal templates
   - 360 feedback basics

6. Training:
   - Course scheduling
   - Completion tracking

7. Self-Service Web:
   - Profile management
   - Leave application
   - Payslip access

8. Reporting:
   - Dashboards and CSV/XLS export.

Project Schedule Overview

The projected timeline for the DHRMS is 21 weeks. To ensure timely delivery while maintaining quality, an additional 3 weeks have been allocated as a contingency buffer. This allowance accounts for potential unforeseen circumstances such as integration challenges, extended user acceptance testing (UAT) feedback cycles, or minor scope refinements identified during development.

Projected Timeline

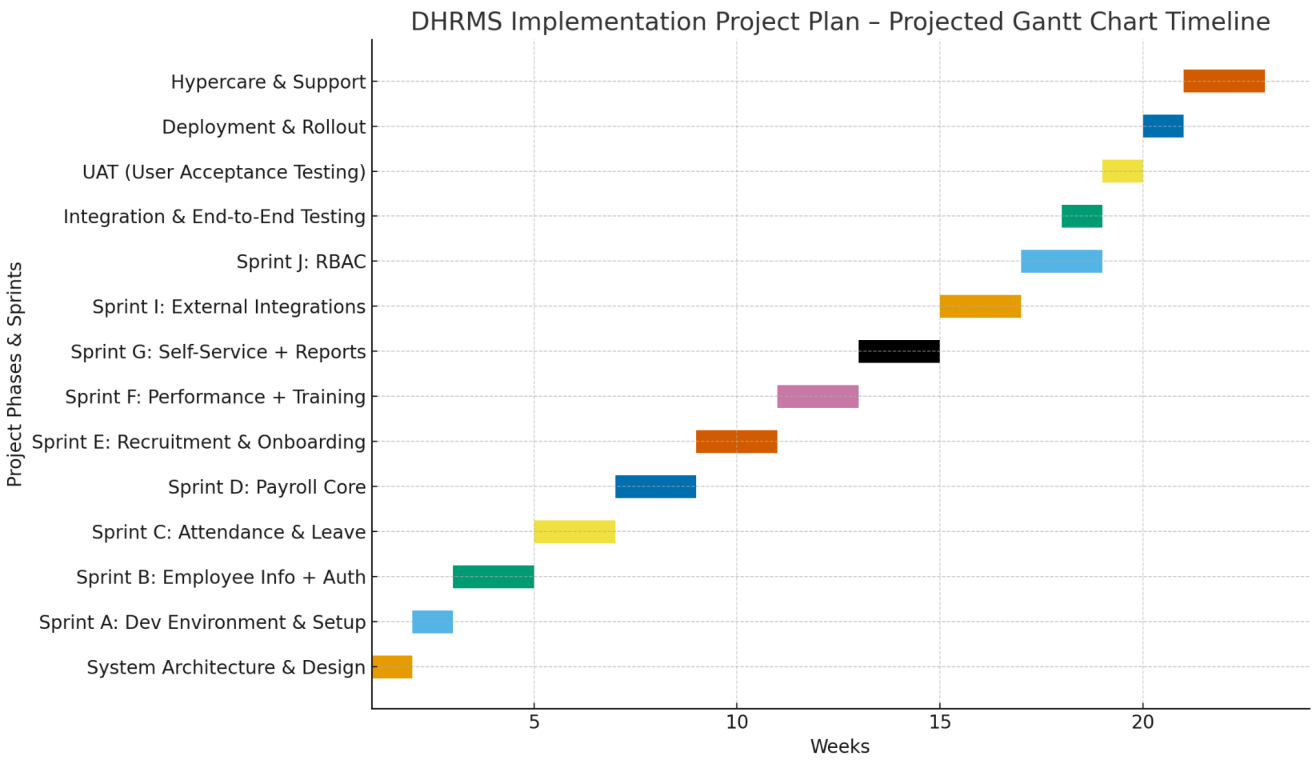

Final Timeline Summary

Targeted Project Duration: 21 weeks
Project Duration + Contingency Buffer: 24 weeks

Project Closure & Conclusion

Project Recap & Final Deliverable

Upon successful completion of this 21-week project plan, the Datafin Human Resource Management System (DHRMS) will be fully deployed and operational in the production environment. The final deliverable is a centralized, web-based HRMS that automates all core HR functions as specified, including Employee Management, Recruitment, Attendance, Payroll, Performance, and Training, accessible via a secure Employee Self-Service Portal.

Success Criteria

Project success will be measured against the following criteria:

- All core modules are developed, integrated, and functioning as per the system description
- On-Time Delivery by the end of Week 21 in the absence of unforeseen circumstances.

- Formal sign-off is received from HR and management stakeholders following the UAT phase.
- The application passes all smoke tests post-deployment and operates without critical issues during the initial hypercare period.

Following this milestone, the project will be formally closed, and the system will enter the ongoing Hypercare & Post-Deployment Support phase.
